

Date: 5/24/2004 12:54 PM (b)(6)
Sender: (b)(6)
Priority: Normal
Subject: FW: TCA PDT Agenda For 25 May 2004 (b)(6)
Author: (b)(6)
Date: 5/24/2004 12:54:00 PM

(b) (6)

cc: (b)(6)
Subject: FW: TCA PDT Agenda For 25 May 2004

Reminder.....

(b) (6)

Subject: TCA PDT Agenda For 25 May 2004
Please find attached the agenda for the Tucson Sector PDT meeting to be held at the Tucson Station (Swan Entrance to Davis Monthan AFB) starting at 10:00 on Tuesday the 25th.....
Conference call in number is: (b) (7)(E)
For those in the EWG a meeting will begin at 8:30.....

<<052504AD.pdf>>

(b)(6)

Senior Project Manager

(b)(6)



052504AD.PDF

**BORDER BARRIER SYSTEM PROGRAM MANAGEMENT
DEPARTMENT OF HOMELAND SECURITY
BUREAU OF CUSTOMS AND BORDER PROTECTION
TUCSON SECTOR - U.S. BORDER PATROL**

MEETING AGENDA

Meeting Date and Time: 25 May 2004, 10:00 am
Meeting Location: Tucson Station

MEETING PURPOSE

TCA PDT Meeting

INTRODUCTIONS

10:00 – 10:15 REVIEW OF ACTION ITEMS

ACTION	RESPONSIBLE
1. Follow up on contract for GSRC to prepare EA for RVS in Douglas AO - AERC still has not received any funding for Douglas/Wilcox RVS project. (b)(6) will follow up with HQ BOR to determine status. (b)(6)	(b)(6)
2. Lighting design test follow up with Castro Electric. Scope for Baker Design.	
3. Ephraim Ridge Report	
4. Move the 1" HDPEP waterline in Naco	
5. 100% Naco 10 mile 22 June 2004	
6. 100% remainder of 5 miles DGL East of POE 27 May 2004	
7. Asphaltic Concrete arranged for August National Guard deployment	
8. BOM and order for USBP landing mat fence construction in DGL	
9. 3.6 Miles Douglas comments due 11 May	
10. Corridor Report comments due 11 May	
11. 15% Nogales Design due 11 May	
12. SOW for GSRC to do a Phase I on Ephraim Ridge property	
ACTION	
Environmental Working Group	
1. San Pedro engineering recommendations, due 11 May	
2. Copies of UAV environmental documents for JTF-6 missions to (b)(6)	
3. Narrow down options on San Pedro water mitigation plans	
4. WWD 404 permit mitigation plan – GSRC contract to contracting.	

*See
mitt to speak
to me
re: 6E info
padding to track
plan*

10:15 – 10:20 RVS

No report from IMC

10:20 – 10:45 MILITARY DEPLOYMENTS

**BORDER BARRIER SYSTEM PROGRAM MANAGEMENT
DEPARTMENT OF HOMELAND SECURITY
BUREAU OF CUSTOMS AND BORDER PROTECTION
TUCSON SECTOR - U.S. BORDER PATROL**

Task Name	FY04 TUCSON SECTOR DEPLOYMENTS											
	2nd Quarter			3rd Quarter			4th Quarter					
Naco, Az	Feb	Mar	Apr	May	Jun	Jul	Aug					
JTF-6 (MWSS 272 - LWC/Road/Bollard Fence) JT-3708-0	[Solid bar from Feb to Aug]											
JTF-6 (917th Prime Beef - 2 Miles Primary Fence) JT-3998-04												
JTF-6 (MWSS 371 - 4 Caps for the LWC's) JT-4070-04												
Douglas, Az East of POE	[Solid bar from Feb to Aug]											
JTF-6 (B Co, 8th ESB - 1.5 Miles of Road) JT-2795-04												
JTF-6 (MWSS 373 - LWC's 10, 11 & 12) JT-4070-04												
Nogales, Az												
JTF-6 (854th En. Bn. - Cbt/Hvy) JT-2793-04												
Douglas, Az (Whitewater Draw - West of POE)												
Oregon National Guard 2 - 2 week deployments												
Alaska National Guard												
Douglas, Az (West of POE)												
Illinois National Guard (LWCs @ King Ranch Rd.)												

Arizona National Guard

(b)(6)

WWD - West of DGL POE

- Oregon National Guard - June 2004, 30 soldiers for two 2-week deployments
- Alaska National Guard - 15 soldiers, 1 to 15 May 2004 (Completed)

Douglas Roadway West of POE

- Illinois N.G. 10 July 2004 (70 troops, LWCs on Kings Ranch Road - possible backup on WWD)

JTF-6

(b)(6)


Scheduled Deployments FY'04

- Naco (Fence & Barriers) 917th Prime Beef Squadron 1 May - 18 Jun (Underway)
- Douglas (Low-water crossings and Bollard Fence) MWSS 373 1-30 Jun
- Naco (Low-water crossings) MWSS 371 6 Jul - 6 Aug (b)(6)
- Nogales, Az USBP (Patrol Roads) 10 Jul - 23 Aug


10:45 - 11:15 ENGINEERING

- Baker Eng. - updates, discussion and map of projects
 - Douglas, 13 Miles of Roadway
 - Douglas, Lighting
 - Douglas, Construction Oversight, and Staking.
 - Douglas, International Ditch, Preliminary and Final Design

**BORDER BARRIER SYSTEM PROGRAM MANAGEMENT
DEPARTMENT OF HOMELAND SECURITY
BUREAU OF CUSTOMS AND BORDER PROTECTION
TUCSON SECTOR - U.S. BORDER PATROL**

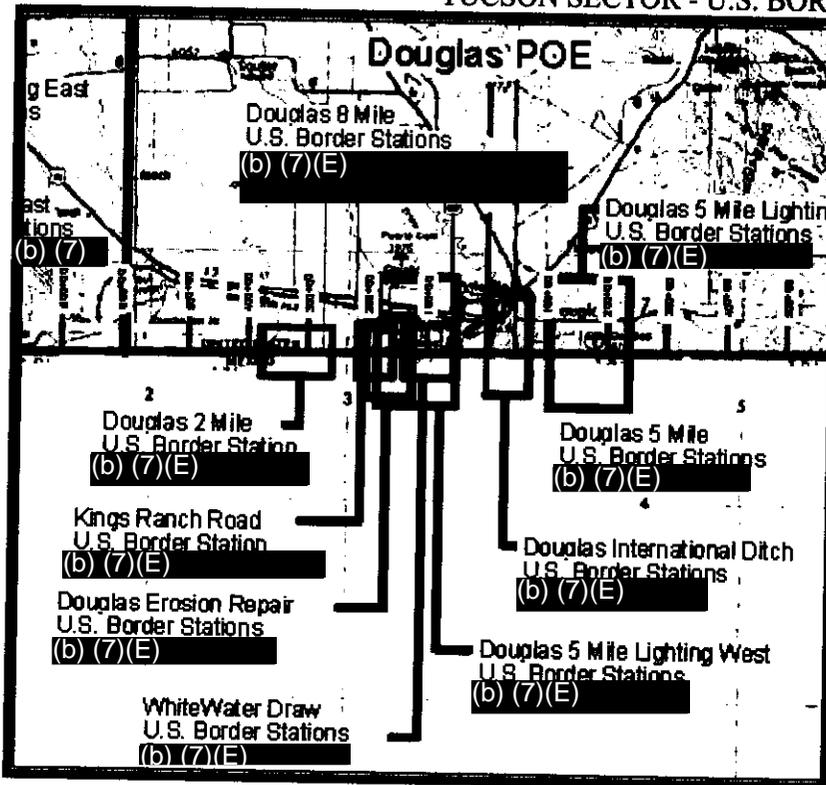


Naco, Lighting (5 Miles) Split East and West of the POE,
 Naco, Primary Fencing, Preliminary and Final Design
 Naco, Construction Oversight and Staking
 Naco, 10-miles Roadway, Preliminary and Final Design

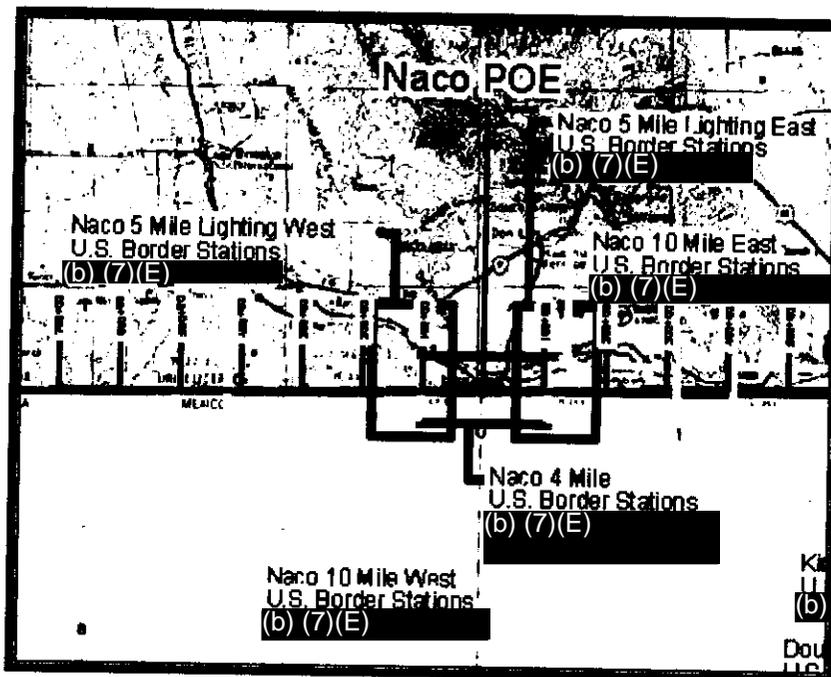

**BORDER BARRIER SYSTEM PROGRAM MANAGEMENT
DEPARTMENT OF HOMELAND SECURITY
BUREAU OF CUSTOMS AND BORDER PROTECTION
TUCSON SECTOR - U.S. BORDER PATROL**

Nogales, 1-1/2 Miles Roadway
Nogales, Construction Oversight and Staking
Nogales, Aerial West of Nogales
Nogales, Schematic Design

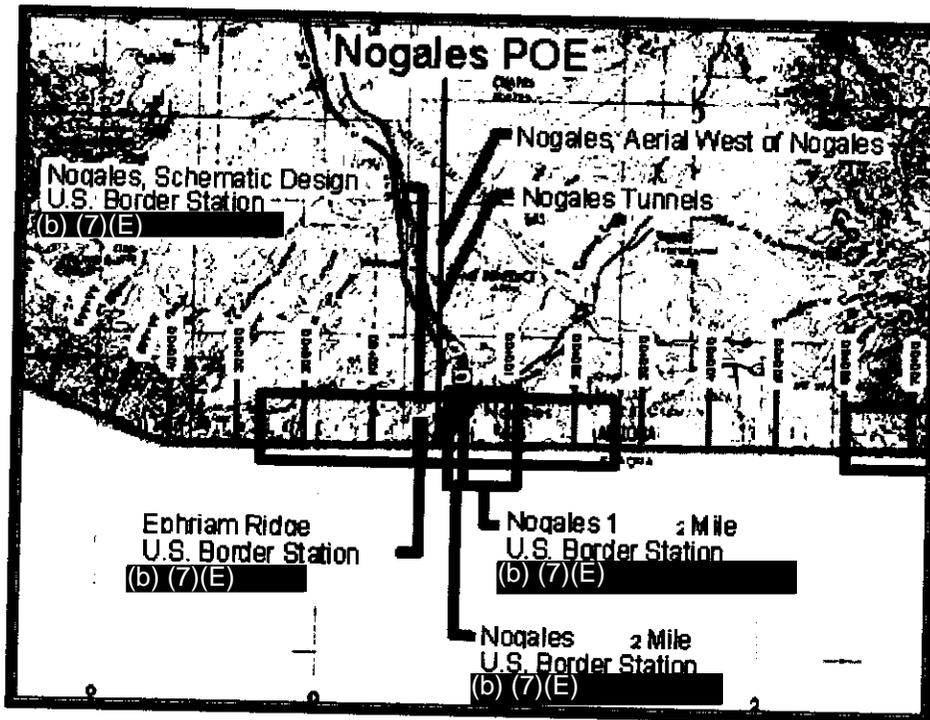

Sonoita, Preliminary Design (map not shown)
Permanent Survey Markers (all stations)
Temporary Vehicle Barriers (all stations)

11:15 – 12:00 ENVIRONMENTAL

- GSRC - updates and discussion
- PEIS Tucson & Yuma (AERC 225)
- BA – Operations – Tucson & Yuma (AERC 51)
- Whitewater Draw 404 Permit
- Checkpoint (b)(7)(E) (AERC 227)
- Checkpoints (b)(7)(E) (AERC 499)
- Naco BA
- Temporary Vehicle Barriers (AJO, TUC, CAG, NGL, & Son Stations)
- Nogales Schematic Design
- RVS EA for Tucson and Ajo Station
- (b)(6) Cabeza Prieta Road Report
- ESA for the Ajo garage

**BORDER BARRIER SYSTEM PROGRAM MANAGEMENT
DEPARTMENT OF HOMELAND SECURITY
BUREAU OF CUSTOMS AND BORDER PROTECTION
TUCSON SECTOR - U.S. BORDER PATROL**

12:00 – 1:00 LUNCH

1:00 – 1:30 REAL ESTATE

USACE – (b)(6)

Douglas Lighting (5 Miles) Split East and West of the POE

Douglas, 13-Miles Roadway West of POE

Douglas, International Ditch

Naco, Lighting (5 Miles) Split East and West of the POE

Nogales, 2-Miles Roadway East of POE

Nogales, Construction & ROW Acquisition

Nogales, Schematic Design

Sonoita, Preliminary Design, and Coordination

Permanent Survey Markers

Temporary Vehicle Barriers

(b)(6)

Ephraim Ridge Reclamation

1:30 – 1:45 PROCUREMENT

Naco & Douglas deployments (JTF-6)

Follow-up on Whitewater Draw (National Guard)

1:45 – 2:00 CONSTRUCTION

Follow-up on Whitewater Draw by Kleinfelder

OTHER ITEMS

NEXT MEETINGS

22 June 2004 – HDR Phoenix, 10:00 am

27 July 2004 – Tucson Station, 10:00 am

24 August 2004 – HDR Phoenix, 10:00 am

14 September 2004 – Tucson Station, 10:00 am



Tucson PPT 7/25/04

①

EWG sub meeting

- 1) costs for can beho ~~not~~ recommendations
- options for bridges - rock headlets or gabion head options
- & (b) (4) for heavily bridge
- & (b) (4) Oakison
- & (b) (4) low water

BA schedule needs to focus on 1 alternative

- * DOI => decided not negotiated
- => don't know what they want to do
- => bakes did drawing

Should be completed projects

organ pipe & Cabeza Prieta

24" x 36"

3.4d

2) not received UAW request yet

3) On Hold partly personnel etc's

4) WWP - ^{USACE} Robert Summers not identify city of Douglas - report will identify others as partners others okay

^{1st} PETS Tucson (Yuma - wait on UAWs

- operation of stations expanded

} wait on ~~USACE~~

- deadline 28 May 2004

Has sensor info

UAW done take out private land ownership

nutrient ~~see~~ probably more costly than silicon nutrient cost

Effluent ~~litig~~

Chad ~~ford~~ (b) (7)(E) - original BA done - relocate to PMGW near border
- GSKC has not been entered

Chad ~~ford~~ (b) (7)(E) - done

(b) (7)(E)



5/25/04

②

EL06 - Cont:

~~NAAC~~ NAAC GA - SPKunig

Temp vehicle permits - ~~By~~ draft out yesterday

- Sonoran / Nogales / Tucson AOs

Permit ~~to~~ on Casa Grande & Ajo on TOW

Kevin comments June 15

Nogales Schuster Design - was due 5/11/04 15%

- no received

RVS - Tucson & Ajo Station - EA need access roads & foot paths, EOE

3 parts confusion - private or BLM ownership

Cajon Lutea road report - done for 5 miles

- Reviewer of work not under contract

- Requested on the copy of report

4

- (b)(6) has said yes (no on report)

* - GA Requiril - Team decision

Ajo Garage - Phase I ESA

Ephraim Ridge - needs ^{Phase I} EA for land acquisition

Douglas/Wildcat RVS no word - no funds

PDT Meeting @ 10:00 am

Action items

1) Douglas RVS - EA pending

2) Highway design - Castro working on design contract

3) Ephraim Ridge - Plat still waiting on USACE approval

4) Title move lower and re-install

No private person is getting benefit from moving line

w/ N 60' lowcut Proclamation lands

- Title of ownership needs to be checked

- When did go out of ownership - if prior to 1907

5/26/1

7) AC on (b)(6) credit card



⑧ Leading out fence on order since 1 June 2004
take control by BP
Pulled fence by JTF-6

12) SOW for Ephraim bridge - done

RVS - (b)(6)

no monthly reports last couple months
TD funding has stopped - contract issues w/ GSA
NACO & budgets pending
Contract expends Sept 29, 2004
Agreement between LCI & BP
Naco 7 new sites - all addressed in SA
Ag state to correct land agreement wording
Tucson stations not started because of roads location & ownership
Nogales litigation - 15 sites void w/ just analysis ?
pg 5 of 6 change no funds @ AERC for work

Stations - no news

Military Requirements

AZ Nat Guard

WWD started last week

Alaska NB 90% complete on construction

water is flowing by footing & ariz well

Exceeded capacity of 50 Ton crane

Pulled Fence for Posters

Illinois - in July

steel cut press Thursday last week went up 3 times



(4)

JTF-6

- Naco - June before on ground
 - but hard digging
- Nogales - advanced party present
 - surveys scheduled prior to June 2
- Nogales - hotels on site

~~Geography~~

- Nogales -
- Naco -
- Nogales - schematic designs

Environment

- See previous notes

Real Estate

- Nogales 13 miles - BLM due back 10-15 days
- Nogales 2 miles - why they done for 1/2 mile
 - 1 1/2 " - survey done complete weeks - due land but 4 weeks
 - narrow easement possible
- Soarata - private road issue - 2 property owners report ROE's

Procurement

- June order
- July - needs info

Construction

- WWO - progressing well - difficult construction
