

Rapid Response Contract Timeline

	Jan-17	Feb-17	Mar-17	Apr-17	May-17	Jun-17	Jul-17	Aug-17	Sep-17
Environmental (b) (5) Procure Env and Survey Contracts Outreach (public and land managers) Environmental Surveys Biological & Cultural Report Environmental Stewardship Plan	(b) (5)								
Rapid Response Contract Board of Directors Review and Acceptance Draft Construction RFP Pre-Final & Final RFP Prep/Review* RFP Advertise through Award Design Analysis and Submittal Reviews Construction Period	(b) (5)								

*Includes legal review, comment review, and engineering review.

Please Note: This schedule is draft. Baseline schedule will be developed as a part of the project development team's project requirement document.

USACE and CBP are researching additional construction strategies to reduce durations and result in earlier construction start

Assumptions:

(b) (5)

Rapid Response Contract Timeline

	Jan-17	Feb-17	Mar-17	Apr-17	May-17	Jun-17	Jul-17	Aug-17	Sep-17
Environmental (b) (5) Procure Env and Survey Contracts Outreach (public and land managers) Environmental Surveys Biological & Cultural Report Environmental Stewardship Plan	(b) (5)								
Rapid Response Contract Board of Directors Review and Acceptance Draft Construction RFP Pre-Final & Final RFP Prep/Review* RFP Advertise through Award Design Analysis and Submittal Reviews Construction Period	(b) (5)								

*Includes legal review, comment review, and engineering review.
 Please Note: This schedule is draft. Baseline schedule will be developed as a part of the project development team's project requirement document.
 USACE and CBP are researching additional construction strategies to reduce durations and result in earlier construction start
 Assumptions:

(b) (5)

Example Phase 1 Project

	Jan-17	Feb-17	Mar-17	Apr-17	May-17	Jun-17	Jul-17	Aug-17	Sep-17	Average Timeline (days)
Environmental (b) (5) Procure Env and Survey Contracts Outreach (public and land managers) Environmental Surveys Biological & Cultural Report Environmental Stewardship Plan				(b)	(5)					(b) (5)
Real Estate Site Visit & Tract Ownership Research Right of Entry (ROE) Declaration of Taking Devel. & Review DOJ Files Action & Obtain ROE-S Metes & Bounds Survey & Valuation Acquire Title Insurance Offer to Sell - Private Landowner Declaration of Taking (CBP/USACE/DOJ)				(b)	(5)					
Design and Acquisition A/E RFP Development & Award Draft Construction RFP & Survey Pre-Final & Final RFP Prep/Review* RFP Advertise through Award Complete Design (60,90,100%)				(b)	(5)					

*Includes legal review, comment review, and engineering review.

Please Note: This schedule is draft. Baseline schedule will be developed as a part of the project development team's project requirement document.

USACE and CBP are researching additional construction strategies to reduce durations and result in earlier construction start

Assumptions:

(b) (5)

#	Activity	Start	Finish
1	ENV (b) (5)		
2	Environmental Funds Received		
3	Procurement of ESP & Survey Contracts		
4	Public Outreach		
5	Coordination with Land Managers		
6	Environmental Surveys		
7	Draft Biological & Cultural Report		
8	Draft ESP		
9	Review Draft Biological & Cultural Reports		
10	Final Draft Biological & Cultural Reports		
11	Review Draft ESP Issue Comments		
12	Issue Final ESP		
13	Environmental Clearance		

Duration	Predecessor	Functional Area
		Environmental
		Environmental
30		1 Environmental
30		3 Environmental
7		3 Environmental
14	12 From RE, 4	Environmental
30		6 Environmental
30		6 Environmental
7		8 Environmental
7		9 Environmental
7		10 Environmental
7		11 Environmental
		12 Environmental

#	Activity	Start
1	USBP Phase I Requirements Defined	(b) (5)
2	BPAM GIS Validation of Requirements	
3	Project Team On-site Reconnaissance	
4	Real Estate Planning Funds Received	
5	Tract Ownership Validation Data	(b) (5)
6	Approach for ROE & Exploration	
7	Condemn for ROE	
8	Assemble DT Package	
9	DT Package Reviews (USACE/CBP/DOJ)	
10	File Action (DOJ)	
11	Court Awards Possession for Survey	
12	ROE-S Obtained or Exercise Eminent Domain For Survey	
13	Metes & Bounds Survey (Aliquot)	
14	Valuation	
15	Acquire Title Insurance	
16	Real Estate Acquisition Funds Received	
17	Negotiate w/ Land Owner	
18	Secure Offer to Sell	
19	Exercise Eminent Domain	
20	Closing on Offer to Sell	
21	Assemble DT Package	
22	DT Package Reviews (USACE/CBP/DOJ)	
23	Deposit Estimate of Just Compensation w/Court and File Action	
24	Court Awards Possession	
25	Real Estate Certified	

Finish	Duration	Predecessor	Functional Area
(b) (5)			Proj Initiation
(b) (5)			Proj Initiation
(b) (5)			Proj Initiation
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate
(b) (5)			Real Estate

Assumptions

Agency Acceptance of (b) (5)

#	Activity	Start	Finish	Duration
1	PRD Received	(b) (5)	(b) (5)	(b) (5)
2	Draft A/E RFP			
3	A/E RFP Review			
4	Final A/E RFP			
5	A/E IGE			
6	Funds Receipt for Design			
7	Solicit A/E			
8	A/E Proposal Prep			
9	Proposal Received			
10	Proposal Review & Acceptance			
11	Award Package Assembly			
12	Award Package Review			
13	A/E Award			
14	Kickoff			
15	Draft RFP Prep & Survey			
16	Draft RFP Submittal			
17	Draft RFP Review			
18	Comment Review Conference			
19	Pre-Final RFP Prep			
20	Pre-Final RFP Submittal			
21	Pre-Final RFP Review			
22	Comment Review Conference			
23	Final RFP Prep			
24	Final RFP Submittal			
25	Final RFP Review			
26	Funds Received for Construction			
27	Legal Review			
28	Advertise milestone			
29	Advertise period			
30	SSEB			
31	SSEB Report			
32	SSA Report			
33	Prepare Award			
34	CBP CN			
35	D/B Construction Award			
36	Receipt of Bonds			
37	Design Kickoff/NTP			
38	60% Design			
39	60% Design Review			
40	60% Design Comment Resolution			
41	90% Design			
42	90% Design Review			
43	90% Design Comment Resolution			
44	100% Design			
45	100% Design Review & Backcheck			
46	100% Design Acceptance			

- 47 Pre-Construction Meeting
- 48 Mobilization
- 49 Construction Start

(b) (5)

Predecessor	Functional Area	Assumption
	Design & Acq	
	Design & Acq	
	Design & Acq	
	3 Design & Acq	
	3 Design & Acq	
FF (b) (5)	Design & Acq	
5 & 6	Design & Acq	
	7 Design & Acq	
	8 Design & Acq	
	9 Design & Acq	
	10 Design & Acq	
	Design & Acq	
	12 Design & Acq	
	13 Design & Acq	
	14 Design & Acq	
	15 Design & Acq	
	16 Design & Acq	
	17 Design & Acq	
18 & 12(RE)	Design & Acq	
	19 Design & Acq	
	20 Design & Acq	
	21 Design & Acq	
	22 Design & Acq	
	23 Design & Acq	
	24 Design & Acq	
FF (b) (5)	Design & Acq	
	25 Design & Acq	
	27 Design & Acq	
	28 Design & Acq	
	29 Design & Acq	LPTA
	30 Design & Acq	
	31 Design & Acq	
	32 Design & Acq	
	33 Design & Acq	(b) (5)
	34 Design & Acq	
	35 Design & Acq	
	36 Design & Acq	
	37 Design & Acq	
	38 Design & Acq	
	39 Design & Acq	
	40 Design & Acq	
	41 Design & Acq	
	42 Design & Acq	
	43 Design & Acq	
	44 Design & Acq	
	45 Design & Acq	

46 Design & Acq

47 Design & Acq

48 & 25 From RE Design & Acq


#	Activity	Start
1	ENV (b) (5)	(b) (5)
2	Envorinmental Funds Received	
3	Procurement of ESP & Survey Contracts	
4	Public Outreach	
5	Coordination with Land Managers	
6	Environmental Surveys	
7	Draft Biological & Cultural Report	
8	Draft ESP	
9	Review Draft Biological & Cultural Reports	
10	Final Draft Biological & Cultural Reports	
11	Review Draft ESP Issue Comments	
12	Issue Final ESP	
13	Environmental Clearance	

Finish

Duration

Predecessor

Functional Area

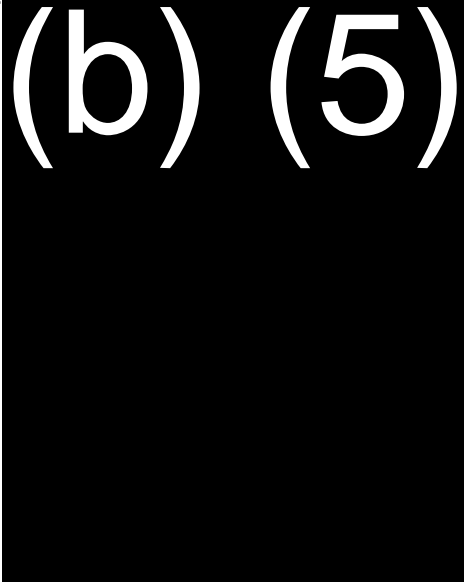

Environmental
Environmental
1 Environmental
Environmental
3 Environmental
Environmental
6 Environmental
6 Environmental
Environmental
Environmental
9 Environmental
Environmental
Environmental

#	Activity	Start
1	ENV (b) (5)	(b) (5)
2	Envorinmental Funds Received	(b) (5)
3	Procurement of ESP & Survey Contracts	(b) (5)
4	Public Outreach	(b) (5)
5	Coordination with Land Managers	(b) (5)
6	Environmental Surveys	(b) (5)
7	Draft Biological & Cultural Report	(b) (5)
8	Draft ESP	(b) (5)
9	Review Draft Biological & Cultural Reports	(b) (5)
10	Final Draft Biological & Cultural Reports	(b) (5)
11	Review Draft ESP Issue Comments	(b) (5)
12	Issue Final ESP	(b) (5)
13	Environmental Clearance	(b) (5)


Finish	Duration	Predecessor	Functional Area
(b)	(5)		Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental

#	Activity	Start
1	USBP Phase I Requirements Defined	(b) (5)
2	BPAM GIS Validation of Requirements	
3	Project Team On-site Reconnaissance	
4	Real Estate Planning Funds Received	
5	Tract Ownership Validation Data	
6	Approach for ROE & Exploration	(b) (5)
7	Condemn for ROE	
8	Assemble DT Package	
9	DT Package Reviews (USACE/CBP/DOJ)	
10	File Action (DOJ)	
11	Court Awards Possession for Survey	
12	ROE-S Obtained or Exercise Eminent Domain For Survey	
13	Metes & Bounds Survey	
14	Valuation	
15	Acquire Title Insurance	
16	Real Estate Acquisition Funds Received	
17	Negotiate w/ Land Owner	
18	Secure Offer to Sell	
19	Exercise Eminent Domain	
20	Closing on Offer to Sell	
21	Assemble DT Package	
22	DT Package Reviews (USACE/CBP/DOJ)	
23	Deposit Estimate of Just Compensation w/Court and File Action	
24	Court Awards Possession	
25	Real Estate Certified	

Finish	Duration	Predecessor	Functional Area
	(b)	(5)	Proj Initiation
			Proj Initiation
			Proj Initiation
	(b)	(5)	Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate
			Real Estate

#	Activity	Start	Finish	Duration
1	PRD Received	(b)	(5)	(5)
2	Draft A/E RFP			
3	A/E RFP Review			
4	Final A/E RFP			
5	A/E IGE			
6	Funds Receipt for Design			
7	Solicit A/E			
8	A/E Proposal Prep			
9	Proposal Received			
10	Proposal Review & Acceptance			
11	Award Package Assembly			
12	Award Package Review			
13	A/E Award			
14	Kickoff			
15	Draft RFP Prep & Survey			
16	Draft RFP Submittal			
17	Draft RFP Review			
18	Comment Review Conference			
19	Pre-Final RFP Prep			
20	Pre-Final RFP Submittal			
21	Pre-Final RFP Review			
22	Comment Review Conference			
23	Final RFP Prep			
24	Final RFP Submittal			
25	Final RFP Review			
26	Funds Received for Construction			
27	Legal Review			
28	Advertise milestone			
29	Advertise period			
30	SSEB			
31	SSEB Report			
32	Discussions			
33	Revised Proposals			
34	SSEB Report			
35	SSA Report			
36	Prepare Award			
37	CBP CN			
38	D/B Construction Award			
39	Receipt of Bonds			
40	Design Kickoff/NTP			
41	60% Design			
42	60% Design Review			
43	60% Design Comment Resolution			
44	90% Design			
45	90% Design Review			
46	90% Design Comment Resolution			

- 47 100% Design
- 48 100% Design Review & Backcheck
- 49 100% Design Acceptance
- 50 Pre-Construction Meeting
- 51 Mobilization
- 52 Construction Start



Predecessor	Functional Area
	Design & Acq
	Design & Acq
	Design & Acq
	Design & Acq
	3 Design & Acq
ff (b) (5)	Design & Acq
5 & 6	Design & Acq
	7 Design & Acq
	8 Design & Acq
	9 Design & Acq
	10 Design & Acq
	Design & Acq
	12 Design & Acq
	13 Design & Acq
	Design & Acq
	15 Design & Acq
	16 Design & Acq
	17 Design & Acq
18 & 12(RE)	Design & Acq
	19 Design & Acq
	20 Design & Acq
	21 Design & Acq
	22 Design & Acq
	23 Design & Acq
	24 Design & Acq
FF (b) (5)	Design & Acq
	25 Design & Acq
	27 Design & Acq
	28 Design & Acq
	29 Design & Acq
	30 Design & Acq
	31 Design & Acq
	32 Design & Acq
	33 Design & Acq
	34 Design & Acq
	35 Design & Acq
	36 Design & Acq
	37 Design & Acq
	38 Design & Acq
	39 Design & Acq
	40 Design & Acq
	41 Design & Acq
	42 Design & Acq
	43 Design & Acq
	44 Design & Acq
	45 Design & Acq

46 Design & Acq

47 Design & Acq

48 Design & Acq

49 Design & Acq

50 Design & Acq

51 & 25 From RE Design & Acq

Example Phase 1 Project

	Jan-17	Feb-17	Mar-17	Apr-17	May-17	Jun-17	Jul-17	Aug-17	Sep-17
Environmental (b) (5) Procure Env and Survey Contracts Outreach (public and land managers) Environmental Surveys Biological & Cultural Report Environmental Stewardship Plan	(b) (5)								
Real Estate Site Visit & Tract Ownership Research Right of Entry (ROE) Declaration of Taking Devel. & Review DOJ Files Action & Obtain ROE-S Metes & Bounds Survey & Valuation Acquire Title Insurance Offer to Sell - Private Landowner Declaration of Taking (CBP/USACE/DOJ)									
Design and Acquisition A/E RFP Development & Award Draft Construction RFP & Survey Pre-Final & Final RFP Prep/Review* RFP Advertise through Award Complete Design (60,90,100%)									

Average
Timeline
(days)
(b) (5)

*Includes legal review, comment review, and engineering review.


Please Note: This schedule is draft. Baseline schedule will be developed as a part of the project development team's project requirement document.

USACE and CBP are researching additional construction strategies to reduce durations and result in earlier construction start

Assumptions:

(b) (5)

#	Activity	Start	Finish
1	ENV (b) (5)		
2	Envorinmental Funds Received		
3	Procurement of ESP & Survey Contracts		
4	Public Outreach		
5	Coordination with Land Managers		
6	Environmental Surveys		
7	Draft Biological & Cultural Report		
8	Draft ESP		
9	Review Draft Biological & Cultural Reports		
10	Final Draft Biological & Cultural Reports		
11	Review Draft ESP Issue Comments		
12	Issue Final ESP		
13	Environmental Clearance		

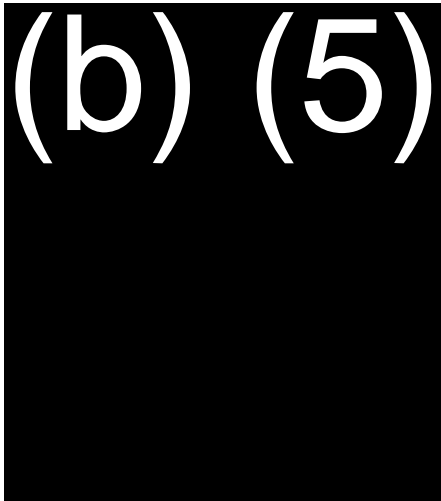

Duration	Predecessor	Functional Area
		Environmental
		Environmental
30		1 Environmental
30		3 Environmental
7		3 Environmental
14	12 From RE, 4	Environmental
30		6 Environmental
30		6 Environmental
7		8 Environmental
7		9 Environmental
7		10 Environmental
7		11 Environmental
		12 Environmental


#	Activity	Start
1	USBP Phase I Requirements Defined	(b) (5)
2	BPAM GIS Validation of Requirements	
3	Project Team On-site Reconnaissance	(b) (5)
4	Real Estate Planning Funds Received	
5	Tract Ownership Validation Data	
6	Approach for ROE & Exploration	(b) (5)
7	Condemn for ROE	
8	Assemble DT Package	(b) (5)
9	DT Package Reviews (USACE/CBP/DOJ)	(b) (5)
10	File Action (DOJ)	(b) (5)
11	Court Awards Possession for Survey	(b) (5)
12	ROE-S Obtained or Exercise Eminent Domain For Survey	(b) (5)
13	Metes & Bounds Survey (Aliquot)	(b) (5)
14	Valuation	(b) (5)
15	Acquire Title Insurance	(b) (5)
16	Real Estate Acquisition Funds Received	(b) (5)
17	Negotiate w/ Land Owner	(b) (5)
18	Secure Offer to Sell	
19	Exercise Eminent Domain	
20	Closing on Offer to Sell	(b) (5)
21	Assemble DT Package	(b) (5)
22	DT Package Reviews (USACE/CBP/DOJ)	(b) (5)
23	Deposit Estimate of Just Compensation w/Court and File Action	(b) (5)
24	Court Awards Possession	
25	Real Estate Certified	

Finish	Duration	Predecessor	Functional Area
(b) (5)	(b) (5)	1	Proj Initiation
(b) (5)	(b) (5)	1	1 Proj Initiation
(b) (5)	(b) (5)	1	Proj Initiation
(b) (5)	(b) (5)	3(FF (b) (5))	Real Estate
(b) (5)	(b) (5)	14	5 Real Estate
(b) (5)	(b) (5)	5 7,8	6 Real Estate
(b) (5)	(b) (5)	10	Real Estate
(b) (5)	(b) (5)	5	9 Real Estate
(b) (5)	(b) (5)	5	10 Real Estate
(b) (5)	(b) (5)	5	11 Real Estate
(b) (5)	(b) (5)		11 Real Estate
(b) (5)	(b) (5)	5	Real Estate
(b) (5)	(b) (5)	15 SS W/13	Real Estate
(b) (5)	(b) (5)	30	13 Real Estate
(b) (5)	(b) (5)	14(FF-(b) (5))	Real Estate
(b) (5)	(b) (5)	14 14,15,16	Real Estate
(b) (5)	(b) (5)		17 Real Estate
(b) (5)	(b) (5)		Real Estate
(b) (5)	(b) (5)	30	18 Real Estate
(b) (5)	(b) (5)	5	19 Real Estate
(b) (5)	(b) (5)	10	21 Real Estate
(b) (5)	(b) (5)	FF (b) (5)	Real Estate
(b) (5)	(b) (5)	FF (b) (5)	Real Estate
(b) (5)	(b) (5)		24 Real Estate

Assumptions

Agency Acceptance of (b) (5)

#	Activity	Start	Finish	Duration
1	PRD Received			
2	Draft A/E RFP			
3	A/E RFP Review			
4	Final A/E RFP			
5	A/E IGE			
6	Funds Receipt for Design			
7	Solicit A/E			
8	A/E Proposal Prep			
9	Proposal Received			
10	Proposal Review & Acceptance			
11	Award Package Assembly			
12	Award Package Review			
13	A/E Award			
14	Kickoff			
15	Draft RFP Prep & Survey			
16	Draft RFP Submittal			
17	Draft RFP Review			
18	Comment Review Conference			
19	Pre-Final RFP Prep			
20	Pre-Final RFP Submittal			
21	Pre-Final RFP Review			
22	Comment Review Conference			
23	Final RFP Prep			
24	Final RFP Submittal			
25	Final RFP Review			
26	Funds Received for Construction			
27	Legal Review			
28	Advertise milestone			
29	Advertise period			
30	SSEB			
31	SSEB Report			
32	SSA Report			
33	Prepare Award			
34	CBP CN			
35	D/B Construction Award			
36	Receipt of Bonds			
37	Design Kickoff/NTP			
38	60% Design			
39	60% Design Review			
40	60% Design Comment Resolution			
41	90% Design			
42	90% Design Review			
43	90% Design Comment Resolution			
44	100% Design			
45	100% Design Review & Backcheck			
46	100% Design Acceptance			

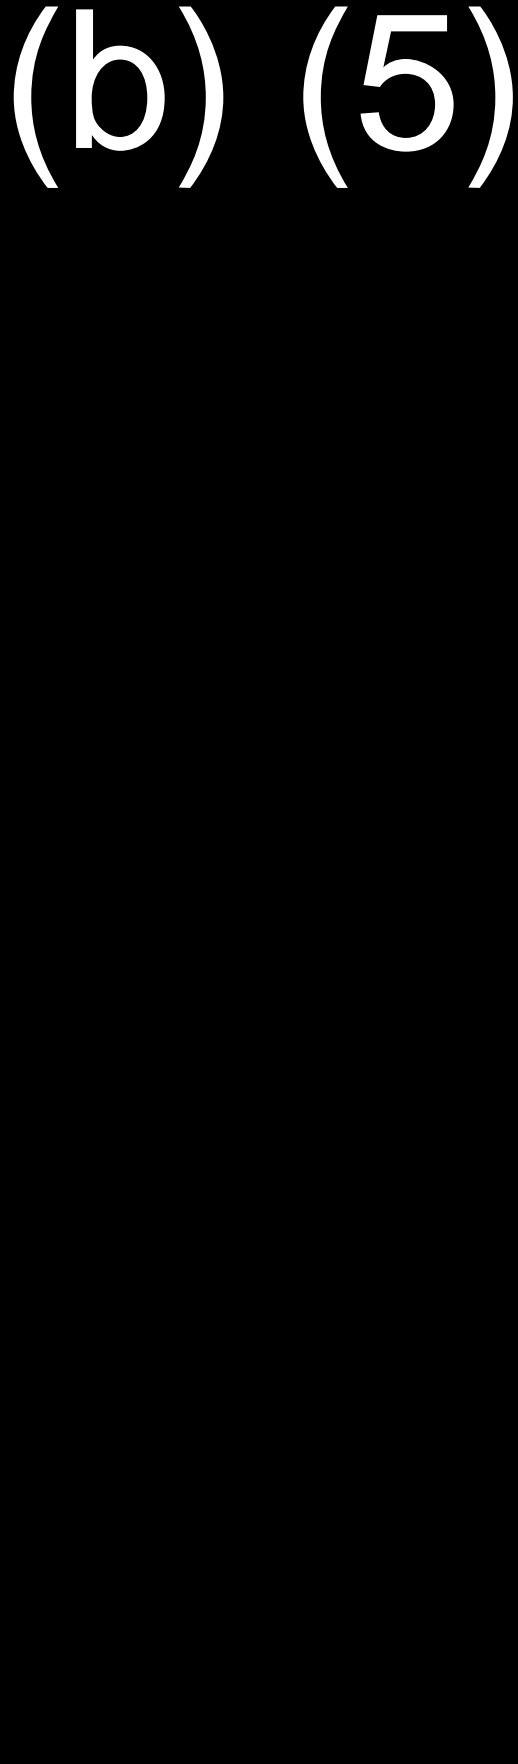

- 47 Pre-Construction Meeting
- 48 Mobilization
- 49 Construction Start

(b) (5)


Predecessor	Functional Area	Assumption
	Design & Acq	
	Design & Acq	
	Design & Acq	
	3 Design & Acq	
	3 Design & Acq	
FF (b) (5)	Design & Acq	
5 & 6	Design & Acq	
	7 Design & Acq	
	8 Design & Acq	
	9 Design & Acq	
	10 Design & Acq	
	Design & Acq	
	12 Design & Acq	
	13 Design & Acq	
	14 Design & Acq	
	15 Design & Acq	
	16 Design & Acq	
	17 Design & Acq	
18 & 12(RE)	Design & Acq	
	19 Design & Acq	
	20 Design & Acq	
	21 Design & Acq	
	22 Design & Acq	
	23 Design & Acq	
	24 Design & Acq	
F (b) (5)	Design & Acq	
	25 Design & Acq	
	27 Design & Acq	
	28 Design & Acq	
	29 Design & Acq	LPTA
	30 Design & Acq	
	31 Design & Acq	
	32 Design & Acq	
	33 Design & Acq	(b) (5)
	34 Design & Acq	
	35 Design & Acq	
	36 Design & Acq	
	37 Design & Acq	
	38 Design & Acq	
	39 Design & Acq	
	40 Design & Acq	
	41 Design & Acq	
	42 Design & Acq	
	43 Design & Acq	
	44 Design & Acq	
	45 Design & Acq	

46 Design & Acq

47 Design & Acq

48 & 25 From RE Design & Acq

#	Activity	Start
1	ENV (b) (5)	(b) (5)
2	Envorinmental Funds Received	
3	Procurement of ESP & Survey Contracts	
4	Public Outreach	
5	Coordination with Land Managers	
6	Environmental Surveys	
7	Draft Biological & Cultural Report	
8	Draft ESP	
9	Review Draft Biological & Cultural Reports	
10	Final Draft Biological & Cultural Reports	
11	Review Draft ESP Issue Comments	
12	Issue Final ESP	
13	Environmental Clearance	

Finish	Duration	Predecessor	Functional Area
	(b)	(5)	Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental
			Environmental

Activity

Start

- 1 USBP Phase I Requirements Defined
- 2 BPAM GIS Validation of Requirements
- 3 Project Team On-site Reconnaissance
- 4 Real Estate Planning Funds Received
- 5 Tract Ownership Validation Data
- 6 Approach for ROE & Exploration
- 7 Condemn for ROE
- 8 Assemble DT Package
- 9 DT Package Reviews (USACE/CBP/DOJ)
- 10 File Action (DOJ)
- 11 Court Awards Possession for Survey
- 12 ROE-S Obtained or Exercise Eminent Domain For Survey
- 13 Metes & Bounds Survey
- 14 Valuation
- 15 Acquire Title Insurance
- 16 Real Estate Acquisition Funds Received
- 17 Negotiate w/ Land Owner
- 18 Secure Offer to Sell
- 19 Exercise Eminent Domain
- 20 Closing on Offer to Sell
- 21 Assemble DT Package
- 22 DT Package Reviews (USACE/CBP/DOJ)
- 23 Deposit Estimate of Just Compensation w/Court and File Action
- 24 Court Awards Possession
- 25 Real Estate Certified

(b) (5)

Finish	Duration	Predecessor	Functional Area
--------	----------	-------------	-----------------

(b)	(5)	Proj Initiation Proj Initiation Proj Initiation
-----	-----	---

(b)	(5)	Real Estate Real Estate
-----	-----	--

#	Activity	Start	Finish	Duration
1	PRD Received	(b) (5)	(5)	(5)
2	Draft A/E RFP			
3	A/E RFP Review			
4	Final A/E RFP			
5	A/E IGE			
6	Funds Receipt for Design			
7	Solicit A/E			
8	A/E Proposal Prep			
9	Proposal Received			
10	Proposal Review & Acceptance			
11	Award Package Assembly			
12	Award Package Review			
13	A/E Award			
14	Kickoff			
15	Draft RFP Prep & Survey			
16	Draft RFP Submittal			
17	Draft RFP Review			
18	Comment Review Conference			
19	Pre-Final RFP Prep			
20	Pre-Final RFP Submittal			
21	Pre-Final RFP Review			
22	Comment Review Conference			
23	Final RFP Prep			
24	Final RFP Submittal			
25	Final RFP Review			
26	Funds Received for Construction			
27	Legal Review			
28	Advertise milestone			
29	Advertise period			
30	SSEB			
31	SSEB Report			
32	Discussions			
33	Revised Proposals			
34	SSEB Report			
35	SSA Report			
36	Prepare Award			
37	CBP CN			
38	D/B Construction Award			
39	Receipt of Bonds			
40	Design Kickoff/NTP			
41	60% Design			
42	60% Design Review			
43	60% Design Comment Resolution			
44	90% Design			
45	90% Design Review			
46	90% Design Comment Resolution			

- 47 100% Design
- 48 100% Design Review & Backcheck
- 49 100% Design Acceptance
- 50 Pre-Construction Meeting
- 51 Mobilization
- 52 Construction Start



Predecessor	Functional Area
	Design & Acq
	Design & Acq
	Design & Acq
	Design & Acq
	3 Design & Acq
ff (b) (5)	Design & Acq
5 & 6	Design & Acq
	7 Design & Acq
	8 Design & Acq
	9 Design & Acq
	10 Design & Acq
	Design & Acq
	12 Design & Acq
	13 Design & Acq
	Design & Acq
	15 Design & Acq
	16 Design & Acq
	17 Design & Acq
18 & 12(RE)	Design & Acq
	19 Design & Acq
	20 Design & Acq
	21 Design & Acq
	22 Design & Acq
	23 Design & Acq
	24 Design & Acq
FF (b) (5)	Design & Acq
	25 Design & Acq
	27 Design & Acq
	28 Design & Acq
	29 Design & Acq
	30 Design & Acq
	31 Design & Acq
	32 Design & Acq
	33 Design & Acq
	34 Design & Acq
	35 Design & Acq
	36 Design & Acq
	37 Design & Acq
	38 Design & Acq
	39 Design & Acq
	40 Design & Acq
	41 Design & Acq
	42 Design & Acq
	43 Design & Acq
	44 Design & Acq
	45 Design & Acq

46 Design & Acq

47 Design & Acq

48 Design & Acq

49 Design & Acq

50 Design & Acq

51 & 25 From RE Design & Acq
